


Lab 2: Agile Backlog Creation and Sprint Simulation in Jira

Problem Statement 41: OpenAPI Mock Server Generator

Name	Sidhant Holla
SRN	PES1UG24AM466
Section	H
Jira project	OpenAPI Mock Server Generator (OMS)

Epics in Jira

All four epics on the project timeline, each showing how much of its work is complete. Epics 1 and 2 are finished, Epic 3 is part-way through Sprint 3, and Epic 4 has been started.

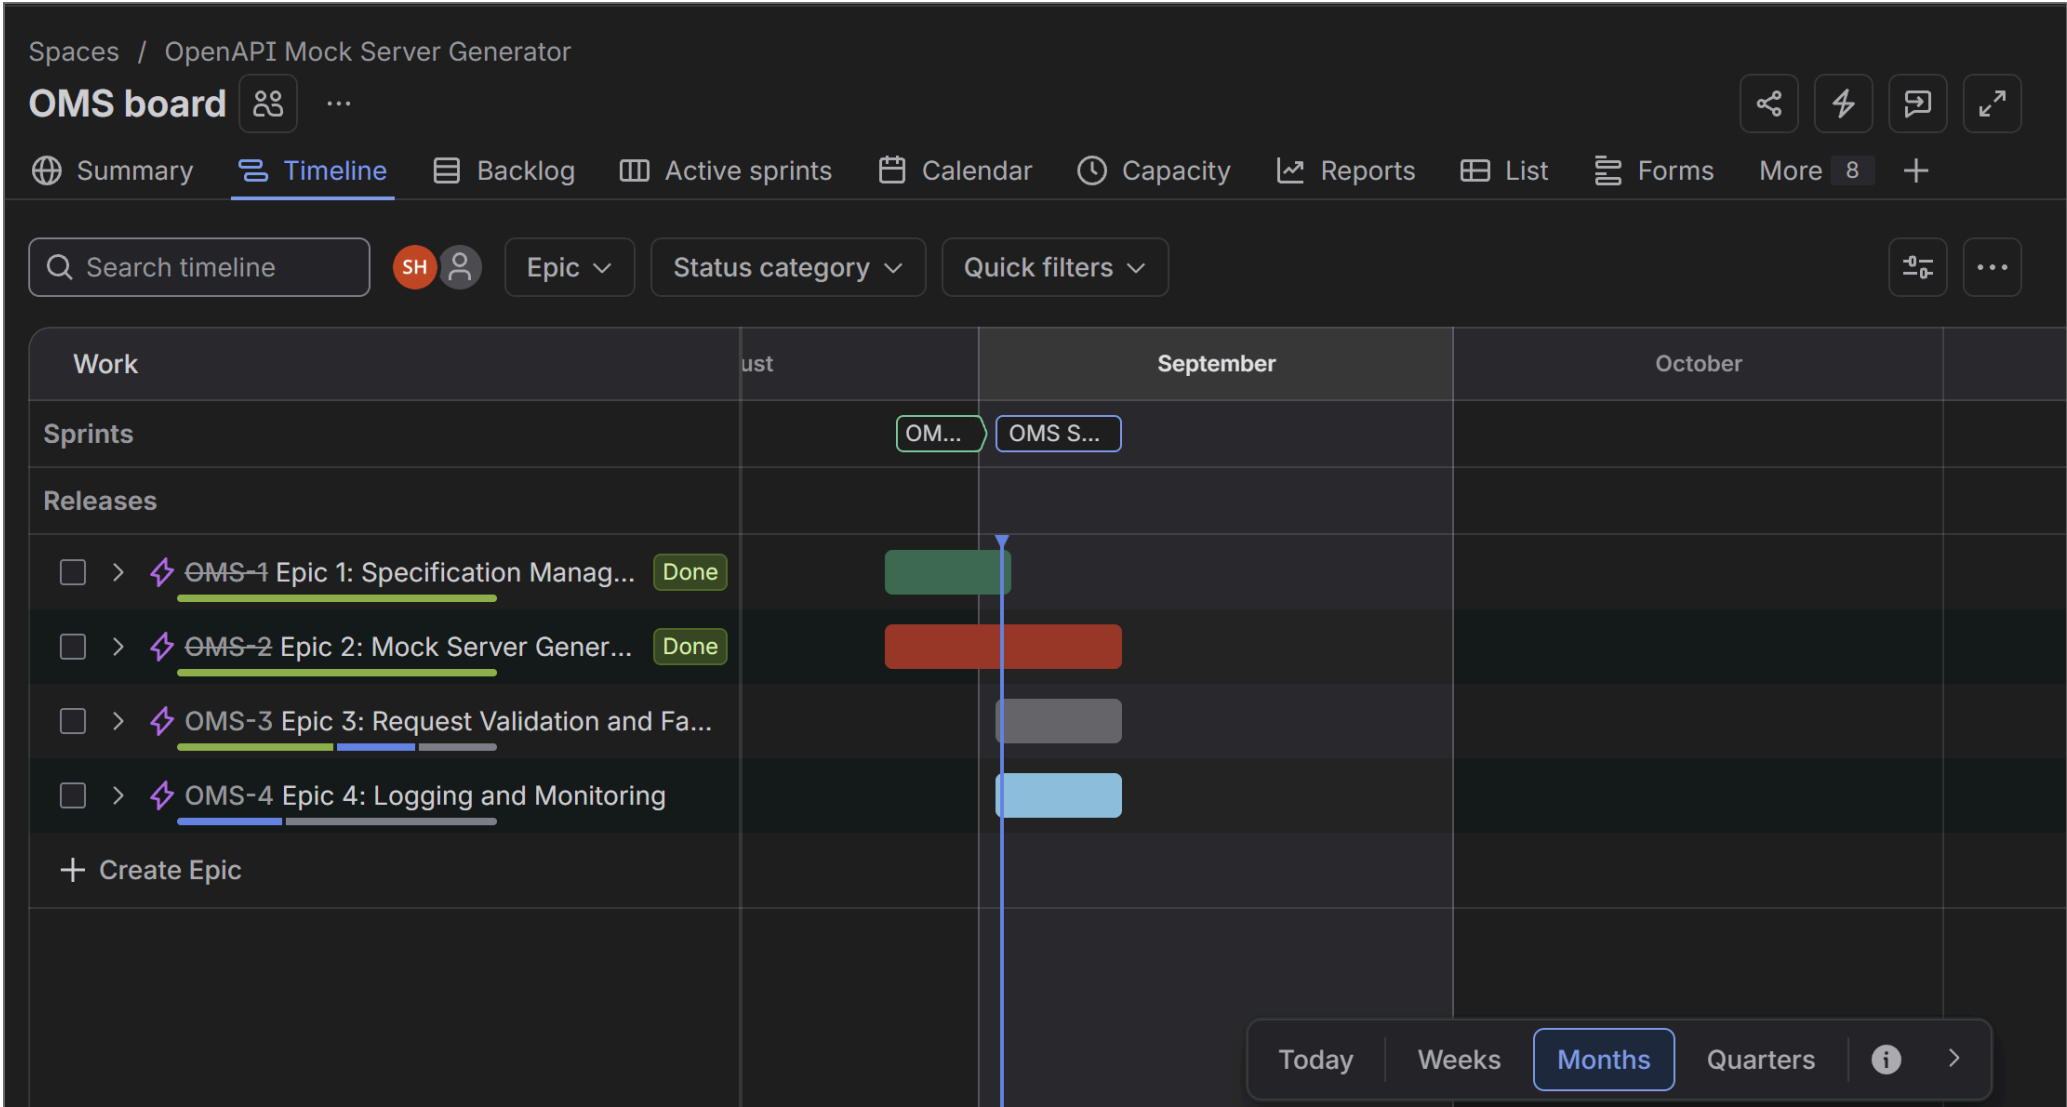

Backlog with Epics and User Stories

The Epic panel on the left lists all four epics. The backlog below shows the user stories grouped under them, with Sprint 3 populated at the top.

Spaces / OpenAPI Mock Server Generator

OMS board

Summary Timeline **Backlog** Active sprints Calendar Capacity Reports List Forms More 8 +

Search backlog SH Version v Epic v Quick filters v

Epic

☒ No epic

☐ Epic 3: Request Validation and Fault Simulation ...

☐ Epic 4: Logging and Monitoring ...

+ Create epic

☐ **OMS Sprint 3** 2 Sep – 9 Sep (3 work items) 2 8 0 Complete sprint ...

Finish the carried-over fault injection work and deliver request logging.

SH ...

☒ OMS-13	Story 3.3: Configure Fault Injection	☐ In Progress v	5	=	SH
☒ OMS-14	Story 3.4: Apply Configuration Without Re...	☐ To Do v	2	>	SH
☒ OMS-15	Story 4.1: Log Every Request	☐ In Progress v	3	=	SH

☐ **Backlog** (2 work items) 4 0 0 Create sprint

☒ OMS-16	Story 4.2: Filter Request Log	☐ To Do v	2	=	SH
☒ OMS-17	Story 4.3: Export Request Log	☐ To Do v	2	>	SH

+ Create


Story Point Assignments

The Sprint 1 report, listing each completed story with the story points assigned to it on the Fibonacci scale. The column header shows the sprint total of 24 points.

Status Report						TIME	* Issue added to sprint after start time
Completed Issues						View in Issue Navigator	
Key	Summary	Issue Type	Priority	Status	Story Points (24)		
OMS-5 *	Story 1.1: Upload Specification File	☒ Story	^ High	DONE	3		
OMS-6 *	Story 1.2: Validate Specification	☒ Story	^ High	DONE	5		
OMS-7 *	Story 1.3: View Validation Errors	☒ Story	^ High	DONE	3		
OMS-8 *	Story 2.1: Generate Mock Endpoints	☒ Story	^ High	DONE	8		
OMS-9 *	Story 2.2: Schema-Compliant Responses	☒ Story	^ High	DONE	5		

Burndown Chart - Sprint 1

Story points remaining across Sprint 1. The grey guideline is the ideal linear burn-down and the red line is the work actually remaining. The sprint was given a one-week window as the lab instructs, while the board itself was worked through inside a single lab session, so the whole 24 points come down together at the right-hand edge instead of in daily steps.

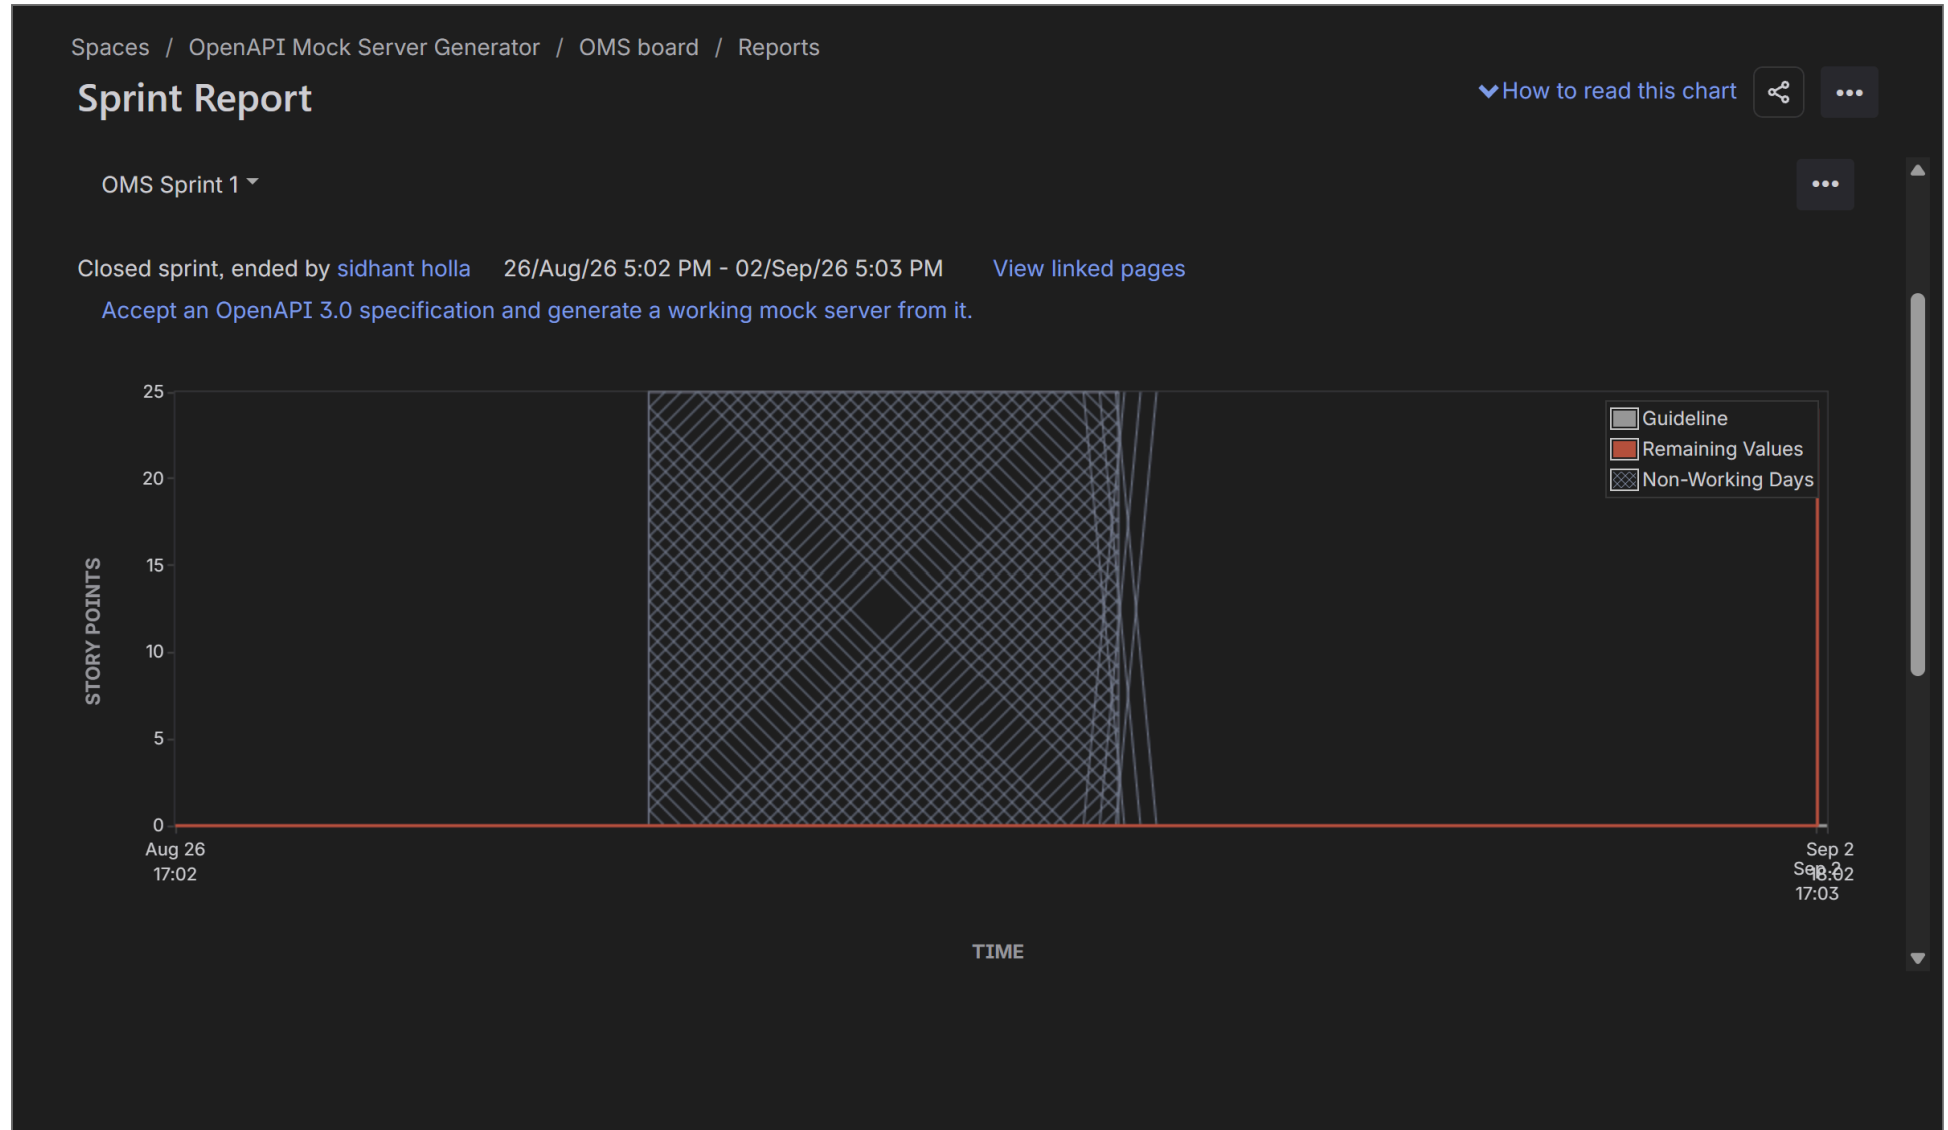

Reflection

Problem Statement 41: OpenAPI Mock Server Generator

Sidhant Holla, PES1UG24AM466, Section H

1. Did your estimations reflect the actual effort?

Mostly, but not everywhere. The five stories in Sprint 1 were estimated at 24 points in total and all of them finished inside the sprint, so those numbers held up. Sprint 2 is where it broke down. Story 3.3, Configure Fault Injection, was given 5 points and did not finish. Looking at it again, that one story bundles three separate pieces of work: a rule editor, a probability engine that decides which requests fail, and the interception that actually swaps the response. Any one of those is a story on its own. An 8 would have been closer to the truth, and splitting it in two would have been better still. The stories that were easy to estimate were the ones with a single clear output, like Export Request Log at 2 points.

2. Was your backlog well-prioritized?

I think so, and the test I used was whether the project would still be worth something if it stopped early. Everything marked High sits in Epics 1 and 2, because the rest of the system depends on it - you cannot validate an incoming request against a schema until you have parsed a specification and generated an endpoint from it. Those all went into Sprint 1 and all got delivered, so after one sprint there was already a working mock server. The Medium and Low items are refinements: filtering the log, exporting it, applying configuration without a restart. Losing any of those would be annoying rather than fatal.

3. How did your simulated sprint align with your plan?

Sprint 1 matched the plan exactly - 24 points committed and 24 delivered. Sprint 2 did not. I committed 16 points, delivered 11, and Story 3.3 rolled back to the backlog and had to be picked up again in Sprint 3. The plan had assumed a steady velocity of around 20 points a sprint, and the second sprint came in well below that. The work itself was not wrong or unnecessary; the estimate on one story was.

4. What insights did the burndown chart give about your team's capacity?

Two things, and the first is really a comment on the simulation rather than on capacity. The line does not come down in steady steps: it holds flat and then falls in a single block at the end. That is because the sprint was given a one-week window, as the lab asks for, while the board was actually worked through inside one session, so every story completes at more or less the same moment. In a real sprint that same shape would be worth acting on, because it would mean too much had been started in parallel and nothing carried through to Done before the next thing was picked up. The second thing is genuine. Delivery went from 24 points in Sprint 1 to 11 in Sprint 2. Two sprints is not enough to call that a velocity, but it is enough to say the 16-point commitment in Sprint 2 was not safe, and it is the reason Sprint 3 was planned at 10 points rather than 16.
